



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	20 Mar '17 M T W T F S S							21
1		MatRev	29 days	Tue 21/03/17	Fri 28/04/17										
2		Sprint1	15 days	Tue 21/03/17	Mon 10/04/17										
3		Designing	11.5 days	Tue 21/03/17	Wed 05/04/17										
4		Designing Color Schemes	1.38 days	Tue 21/03/17	Wed 22/03/17										
5		Main Screen	2 hrs	Tue 21/03/17	Tue 21/03/17		Paulina Binas								
6		Study Screen	2 hrs	Tue 21/03/17	Tue 21/03/17	5	Paulina Binas								
7		Revision Screen	0.25 days	Tue 21/03/17	Tue 21/03/17	6	Arseny Mansyrev								
8		Test Screen	1 hr	Tue 21/03/17	Tue 21/03/17	7	Rupali Sharma								
9		Options Screen	0.25 days	Tue 21/03/17	Wed 22/03/17	8	Paulina Binas								
10		Help Screen	0.25 days	Wed 22/03/17	Wed 22/03/17	9	Arseny Mansyrev								
11		Designing Screens	9.81 days	Wed 22/03/17	Wed 05/04/17	4									
12		Main Screen (Genre Selection)	1 day	Wed 22/03/17	Thu 23/03/17	4	Paulina Binas								
13		Study Screen	1.5 days	Thu 23/03/17	Mon 27/03/17	12									
14		Choose subject	4 hrs	Thu 23/03/17	Fri 24/03/17	12	Rupali Sharma								
15		Scroll through	8 hrs	Fri 24/03/17	Mon 27/03/17	14	Arseny Mansyrev								
16		Revision Screen	2 days	Mon 27/03/17	Wed 29/03/17	13									
17		Choose subject	8 hrs	Mon 27/03/17	Tue 28/03/17	13	Rupali Sharma								
18		Scroll through	8 hrs	Tue 28/03/17	Wed 29/03/17	17	Arseny Mansyrev								

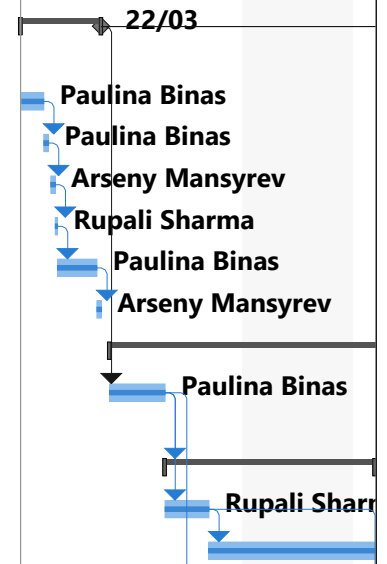

Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predicted	Resource Names	20 Mar '17							21
								M	T	W	T	F	S	S	
19		Test Screen	2.51 days	Wed 29/03/17	Fri 31/03/17	16									
20		Test Screen	8 hrs	Wed 29/03/17	Thu 30/03/17	16	Rupali Sharma								
21		Result Screen	1 day	Thu 30/03/17	Fri 31/03/17	20	Rupali Sharma[50%]								
22		Other Screens	2.5 days	Mon 03/04/17	Wed 05/04/17	19									
23		Options Screen	1 day	Mon 03/04/17	Mon 03/04/17	19	Paulina Binas								
24		Help Screen	1 day	Tue 04/04/17	Wed 05/04/17	23	Arseny Mansyrev								
25		Mockups	12 days	Fri 24/03/17	Mon 10/04/17	4									
26		Main Screen (Genre Selection)	1 day	Fri 24/03/17	Fri 24/03/17	12	Tenzin Choewang								
27		Study Screen	5.48 days	Mon 27/03/17	Mon 03/04/17	13									
28		Choose subject	2 days	Mon 27/03/17	Mon 03/04/17	14	Rupali Sharma								
29		Scroll through	1 day	Tue 28/03/17	Thu 30/03/17	15	Tenzin Choewang								
30		Revision Screen	2.93 days	Wed 29/03/17	Mon 03/04/17	16									
31		Choose subject	1 day	Wed 29/03/17	Thu 30/03/17	17	Tenzin Choewang								
32		Scroll through	1 day	Wed 29/03/17	Mon 03/04/17	18	Tenzin Choewang								
33		Test Screen	2.78 days	Mon 03/04/17	Wed 05/04/17	19									
34		Test Screen	2 days	Mon 03/04/17	Wed 05/04/17	20	Paulina Binas								














Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID	Task Mode	Task Name	Duration	Start	Finish	Predicted	Resource Names	20 Mar '17							21
								M	T	W	T	F	S	S	
35		Result Screen	1 day	Mon 03/04/17	Wed 05/04/17	21	Arseny Mansyrev[50%]								
36		Other Screens	3 days	Thu 06/04/17	Mon 10/04/17	22									
37		Options Screen	2 days	Thu 06/04/17	Fri 07/04/17	23	Tenzin Choewang								
38		Help Screen	2 days	Fri 07/04/17	Mon 10/04/17	24	Tenzin Choewang								
39		Sprint 2	7 days	Tue 11/04/17	Wed 19/04/17	2									
40		Screen Implementation	7 days	Tue 11/04/17	Wed 19/04/17										
41		Main Screen (Genre Selection)	7 days	Tue 11/04/17	Wed 19/04/17		Paulina Binas[75%]								
42		Study Screen	7 days	Tue 11/04/17	Wed 19/04/17										
43		Choose subject	7 days	Tue 11/04/17	Wed 19/04/17		Tenzin Choewang[75%]								
44		Revision Screen	7 days	Tue 11/04/17	Wed 19/04/17										
45		Choose subject	7 days	Tue 11/04/17	Wed 19/04/17		Arseny Mansyrev[75%]								
46		Test Screen	7 days	Tue 11/04/17	Wed 19/04/17										
47		Test Screen	7 days	Tue 11/04/17	Wed 19/04/17		Rupali Sharma[75%]								
48		Sprint 3	7 days	Thu 20/04/17	Fri 28/04/17										
49		Screen Transitions	7 days	Thu 20/04/17	Fri 28/04/17	39									
50		Main Screen	7 days	Thu 20/04/17	Fri 28/04/17										
51		To Study Screen	7 days	Thu 20/04/17	Fri 28/04/17		Tenzin Choewang								
52		To Revision Screen	7 days	Thu 20/04/17	Fri 28/04/17		Rupali Sharma								
53		To Test Screen	7 days	Thu 20/04/17	Fri 28/04/17		Arseny Mansyrev								
54		To Help Screen	7 days	Thu 20/04/17	Fri 28/04/17		Paulina Binas								

Project: MatRev
Date: Sun 23/04/17


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	20 Mar '17							21
								M	T	W	T	F	S	S	
55		To Option Screen	7 days	Thu 20/04/17	Fri 28/04/17		Paulina Binas								
56		Study Screen	7 days	Thu 20/04/17	Fri 28/04/17										
57		Topic List Screen	7 days	Thu 20/04/17	Fri 28/04/17		Tenzin Choewang								
58		Sliders	7 days	Thu 20/04/17	Fri 28/04/17		Paulina Binas								
59		Revision Screen	7 days	Thu 20/04/17	Fri 28/04/17										
60		Topic List Screen	7 days	Thu 20/04/17	Fri 28/04/17		Tenzin Choewang								
61		Sliders	7 days	Thu 20/04/17	Fri 28/04/17		Paulina Binas								
62		Test Screen	7 days	Thu 20/04/17	Fri 28/04/17										
63		Between Questions	7 days	Thu 20/04/17	Fri 28/04/17		Rupali Sharma								
64		To Main Screen	7 days	Thu 20/04/17	Fri 28/04/17		Rupali Sharma								
65		See Wrong Answers Screen	7 days	Thu 20/04/17	Fri 28/04/17		Arseny Mansyrev								

Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


27 Mar '17 03 Apr '17 10 Apr '17 17 Apr '17 24 Apr '17 01 May '17
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T

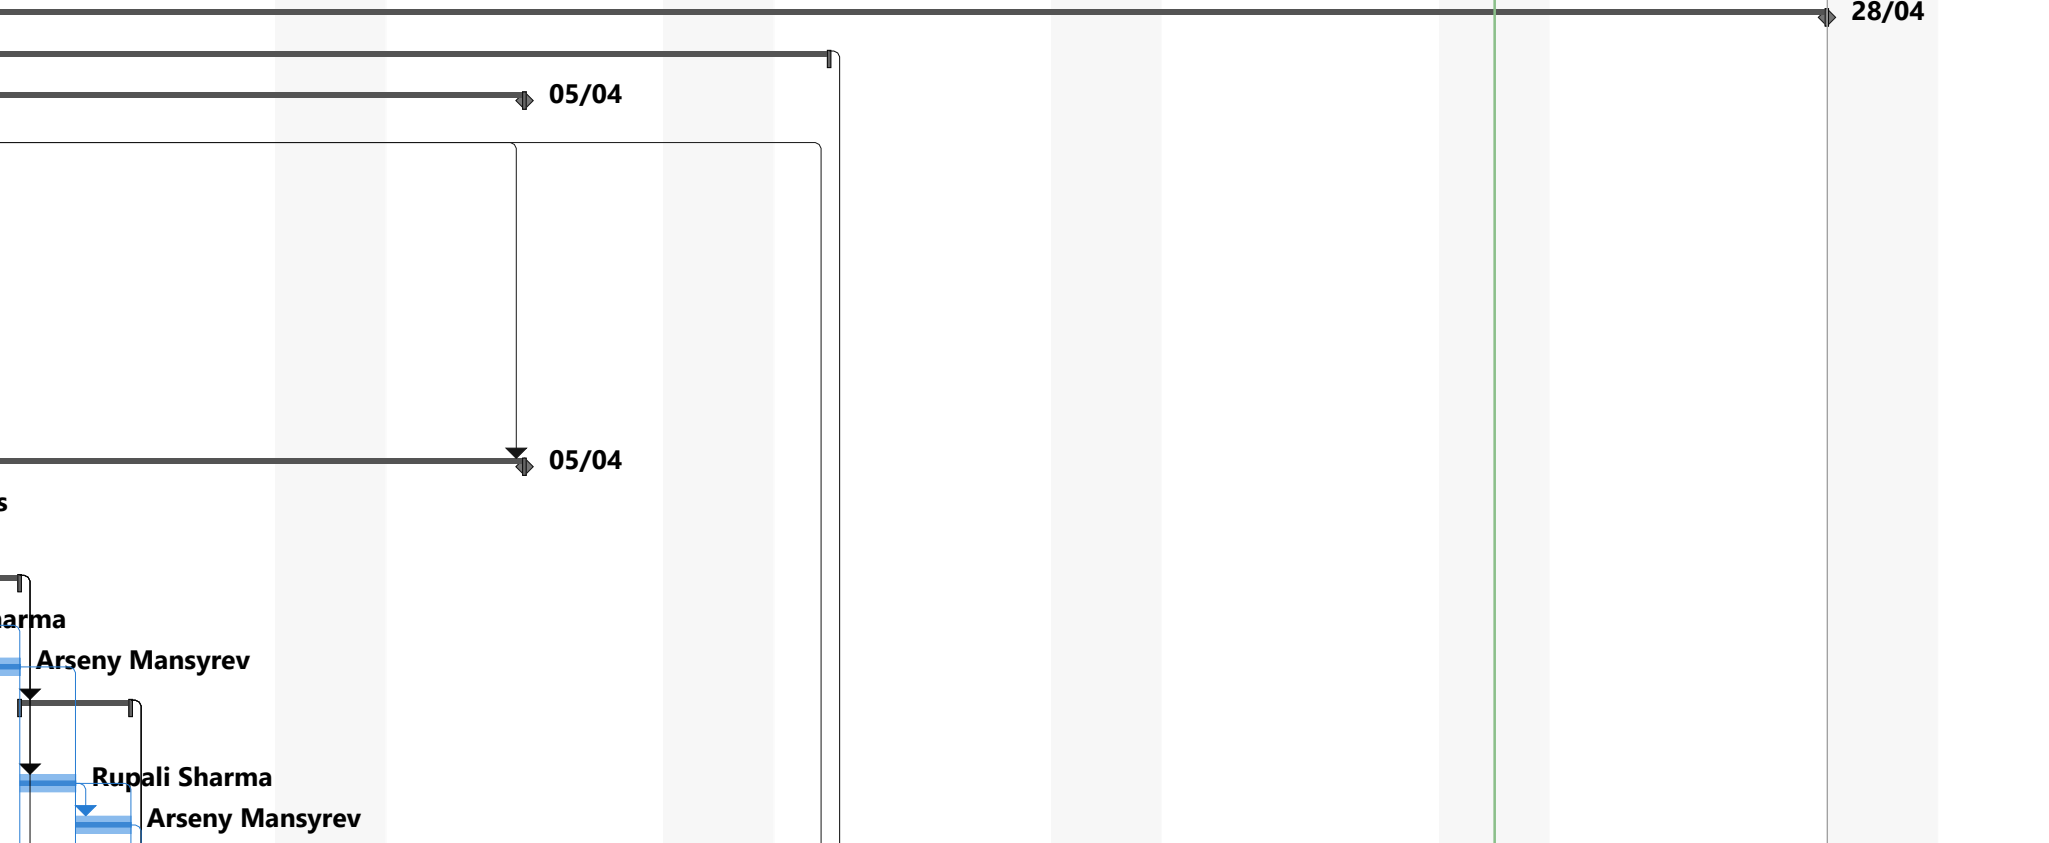

Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


27 Mar '17 M T W T F S S 03 Apr '17 M T W T F S S 10 Apr '17 M T W T F S S 17 Apr '17 M T W T F S S 24 Apr '17 M T W T F S S 01 May '17 M T

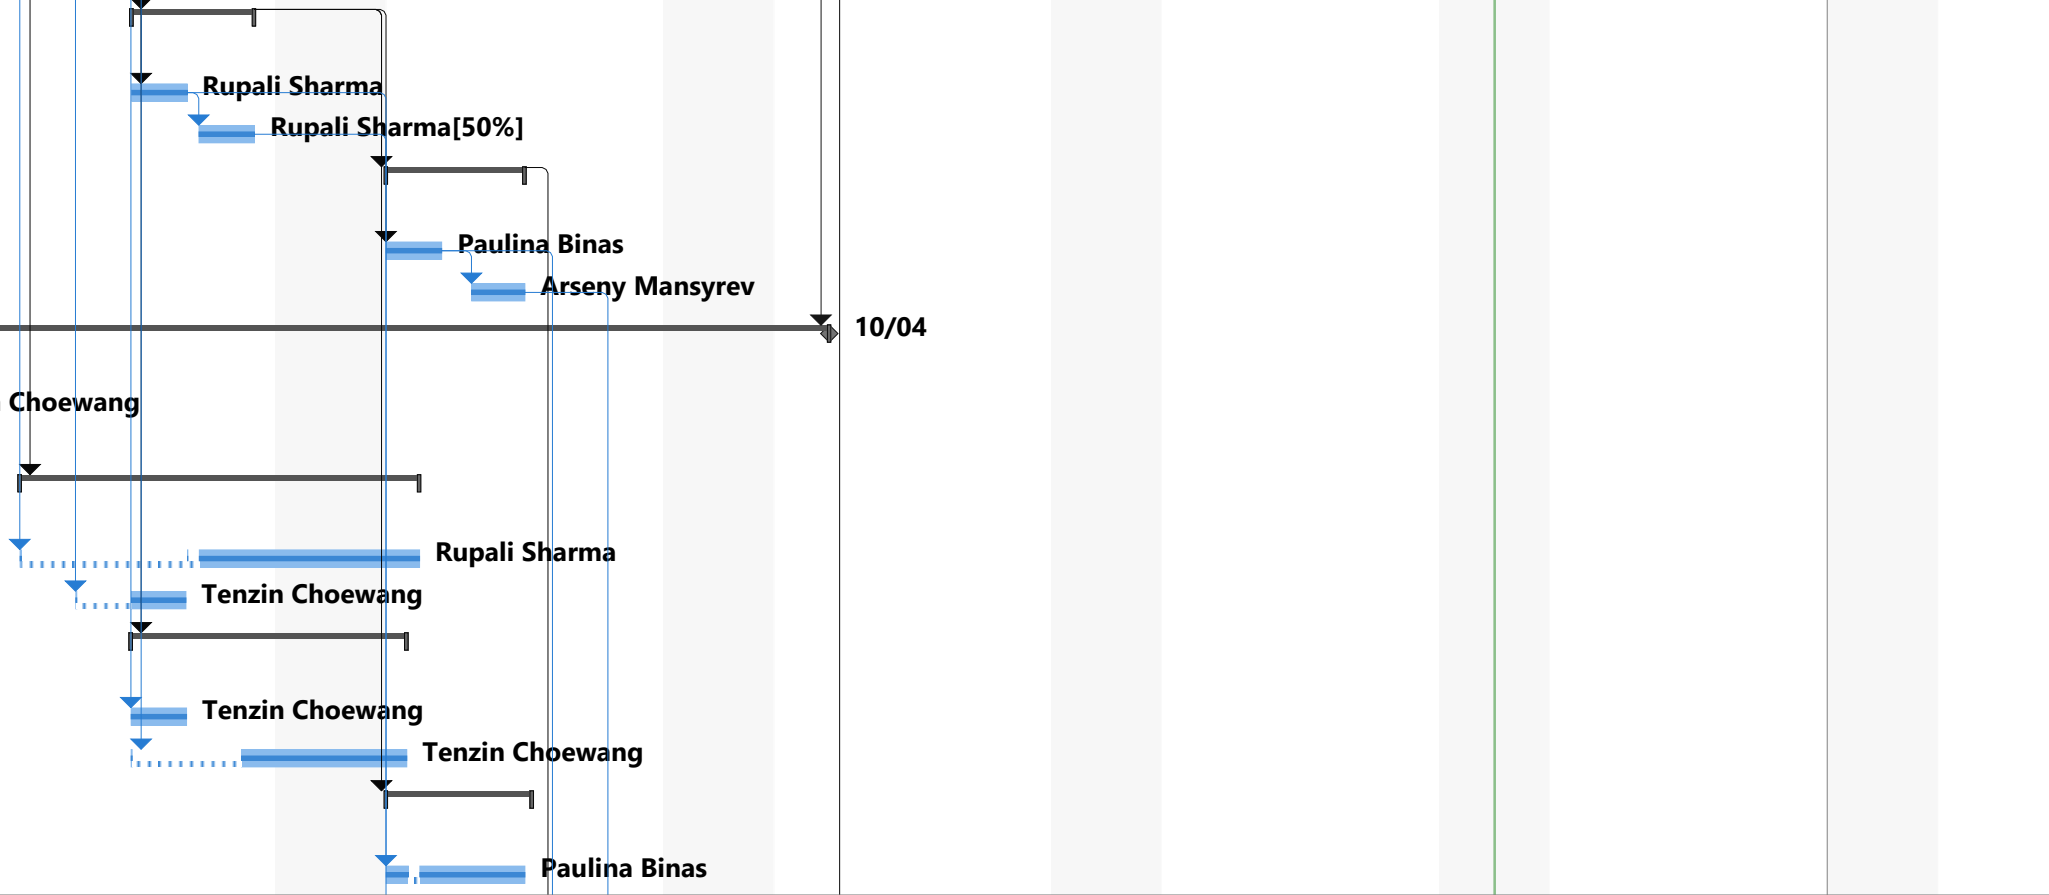

Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

27 Mar '17 03 Apr '17 10 Apr '17 17 Apr '17 24 Apr '17 01 May '17
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T

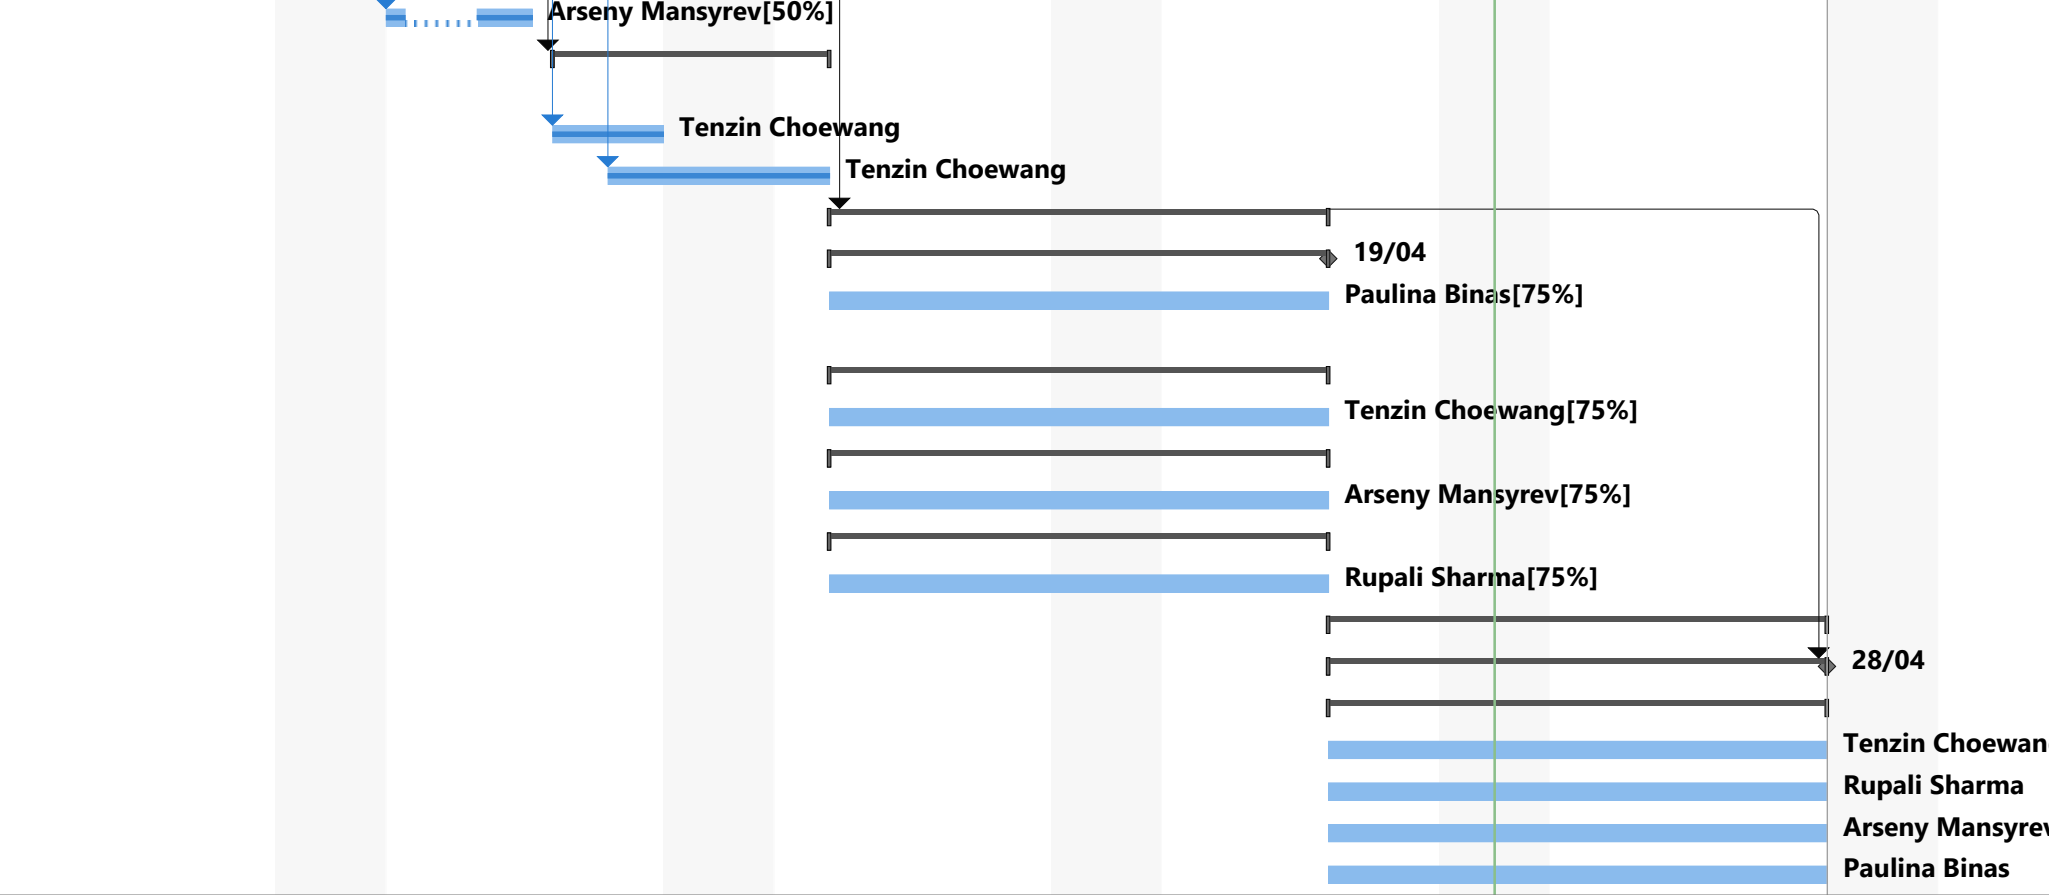

Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

27 Mar '17

M T W T F S S

03 Apr '17

M T W T F S S

10 Apr '17

M T W T F S S

17 Apr '17


M T W T F S S

24 Apr '17

M T W T F S S

01 May '17

M T

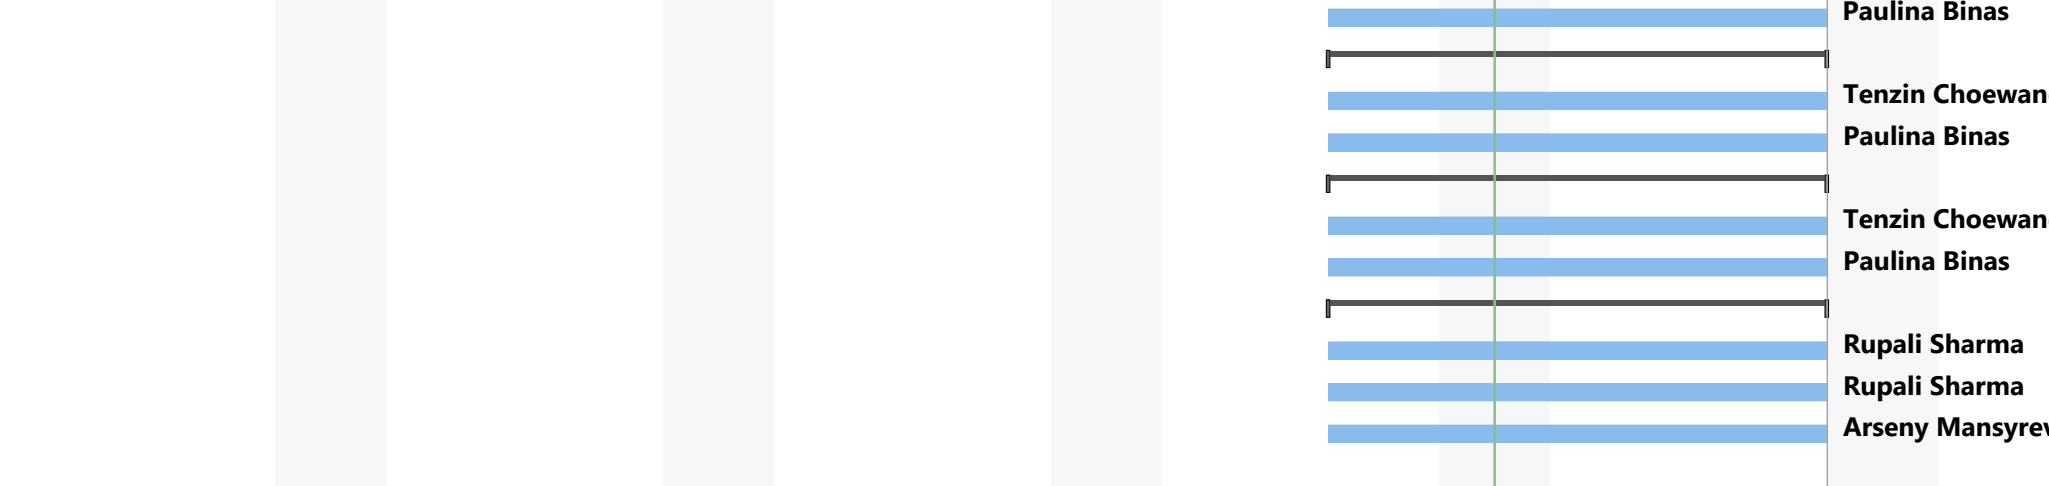

Project: MatRev
Date: Sun 23/04/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
